



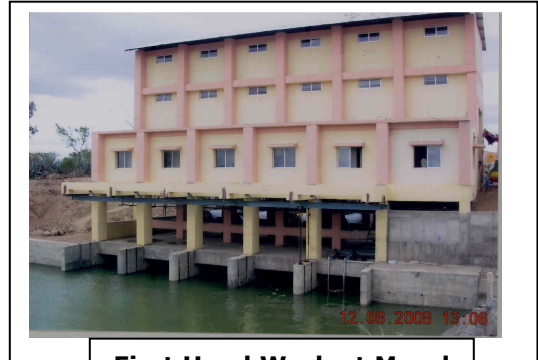

RAMTHAL (MAROL) LIS

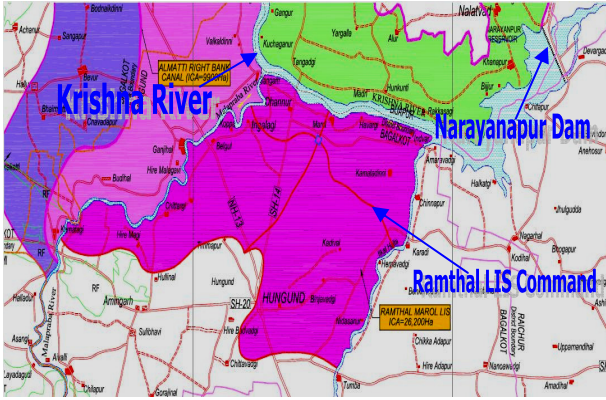

First Head Work at Marol

A) Salient Features:

- **Location** : On the foreshore of Narayanapur Reservoir near Marol village of Hungund taluk.
- **Irrigable Command Area** : 26,200 Ha.
- **Taluks to be benefited** : Hungund Taluk of Bagalkot District.
- **Components of Scheme** :
 - 1st Head Work – At Marol
 - 2nd Head Work – At Ramawadagi

Main Canal :

- 1st Stage - East Canal – 54 KMs
West Canal – 61 KMs
- 2nd Stage – East Canal – 19 KMs
West Canal – 10 KMs
- Hungund Branch Canal – 31 KMs

B) Present Stage of Work

- : 1st Head Work completed.
- : 2nd Head Work nearing completion (turn key)
- : 1st Stage West Canal KM 0.00 to 8.00 completed.
- : 1st Stage West Canal KM 8.00 to 15.00 (nearing completion), KM 15.00 to 21.00 completed & Disty.No.1, 2, 3, 5 & 6 completed.

- C) Expenditure incurred : Rs.48.61 Crores as on Feb '09.
- D) Potential Created : 3,500 Ha.
